ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Comple
1		**NEW ARTS & CULTURE CENTRE**	**785 days?**	**Mon 15/12/2**	**Fri 15/12/28**		**10%**
2		**Governance**	**351 days**	**Mon 16/02/2**	**Mon 21/06/2**		**7%**
3		SAWG Project Review Meeting	1 day	Thu 30/04/26	Thu 30/04/26		100%
4		Public Survey Prep	2 wks	Fri 01/05/26	Thu 14/05/26	3	0%
5		Public Engagement	4 wks	Mon 01/06/2	Fri 26/06/26	3FS+2 wks	0%
6		OBC Preparation	4 wks	Mon 18/05/2	Fri 12/06/26		0%
7		OBC Final paper to SLT	1 day	Mon 22/06/2	Mon 22/06/2	6	0%
8		Final Revised OBC Papers to July '26 Committee	1 day	Mon 22/06/2	Mon 22/06/2		0%
9		*Committee Meeting 2nd July*	0 days	Thu 02/07/26	Thu 02/07/26		0%
10		Establish Project Board	1 wk	Tue 07/07/26	Mon 13/07/2	9	0%
11		Stage 2 Design & Cost review	2 wks	Mon 16/02/2	Fri 27/02/26		100%
12		Stage 3 Design & Cost update	26 days	Fri 03/07/26	Fri 07/08/26		0%
13		Stage 4 Design & Cost					0%
14		FBC - Stage 4 Design & Cost review vs OBC budget	1 wk	Mon 12/10/2	Fri 16/10/26		0%
15		FBC - Operation, function & market expectations (flexibility/profitability) - Client	6 wks	Mon 07/09/26	Fri 16/10/26		0%
16		Council Approval to Final Business Case (OBC Cost Info)	1 day	Thu 22/10/26	Thu 22/10/26	15FS+3 days	0%
17		FBC Cost review at Stage 4 Design	5 days	Mon 08/02/2	Fri 12/02/27	69	0%
18		FBC Cost Review at Tender	1 day	Mon 07/06/2	Mon 07/06/2		0%
19		Tender report & recommendations - PB review vs budget	2 wks	Mon 07/06/2	Fri 18/06/27		0%
20		Project Board agreement to award contract + governance	1 day	Mon 21/06/2	Mon 21/06/2	19	0%
21		Project Board meetings					0%
22		<New Task>					0%
23							0%
24		**Stakeholder Engagement**	**100 days**	**Mon 01/06/2**	**Fri 16/10/26**		**0%**
25		Public Engagement	20 wks	Mon 01/06/2	Fri 16/10/26		0%
26		Museum Trust	20 wks	Mon 01/06/2	Fri 16/10/26		0%
27		Artist Groups	20 wks	Mon 01/06/2	Fri 16/10/26		0%
28		Local businesses	20 wks	Mon 01/06/2	Fri 16/10/26		0%
29		Kiosk operators	20 wks	Mon 01/06/2	Fri 16/10/26		0%
30		Local residents	20 wks	Mon 01/06/2	Fri 16/10/26		0%
31		Schools/colleges	20 wks	Mon 01/06/2	Fri 16/10/26		0%
32							0%
33		**Design Process**	**385 days**	**Mon 15/12/2**	**Fri 04/06/27**		**21%**
34		**Masterplanning Validation**	**24 days**	**Mon 30/03/2**	**Thu 30/04/26**		**100%**
35		Review CAMP Locations	4 wks	Mon 30/03/2	Fri 24/04/26		100%
36		Integrate Culture & Heritage	4 wks	Mon 30/03/2	Fri 24/04/26	35SS	100%
37		Agreement of Proposals SAWG 30/4/26	0 days	Thu 30/04/26	Thu 30/04/26	36FS+4 days	100%
38							0%
39		**Stage 2 Design - Strategic Brief**	**75 days**	**Mon 15/12/2**	**Fri 27/03/26**		**100%**
40		Review & update Brief & Concept design	4 wks	Mon 05/01/2	Fri 30/01/26	9	100%
41		Surveys	8 wks	Mon 19/01/2	Fri 13/03/26		100%
42		Develop Services strategy	9.2 wks	Mon 19/01/2	Mon 23/03/2		100%
43		Develop Sustainability strategy	2 wks	Mon 19/01/2	Fri 30/01/26		100%
44		Intital cost plan	2 wks	Mon 16/02/2	Fri 27/02/26		100%
45		Stage 2 Design Review	2 wks	Mon 16/02/2	Fri 27/02/26	44	100%
46							0%
47		**Stage 3 Design - Spatial Coordination Updated Design**	**130 days**	**Mon 16/02/2**	**Fri 14/08/26**		**53%**
48		Develop architectural design for Planning	2 wks	Mon 06/07/2	Fri 17/07/26	45	75%
49		Services strategy outline design	3 wks	Mon 06/07/2	Fri 24/07/26		75%
50		Structural strategy outline design	3 wks	Mon 06/07/2	Fri 24/07/26		50%
51		Sustainability outline design (Net Zero viability)	1 wk	Mon 06/07/2	Fri 10/07/26		75%
52		Landscape outline design	2 wks	Mon 06/07/2	Fri 17/07/26		0%
53		Surveys	85 days	Mon 02/03/2	Fri 26/06/26		90%
54		Fire Strategy	2 wks	Mon 06/07/2	Fri 17/07/26		0%
55		Stage 3 Design & cost review	4 wks	Mon 06/07/2	Fri 31/07/26		0%
56		Agreement to submit Planning application	1 day	Mon 10/08/2	Mon 10/08/2	9	0%
57		Final Stage 3 design Information	6 wks	Mon 06/07/2	Fri 14/08/26		0%

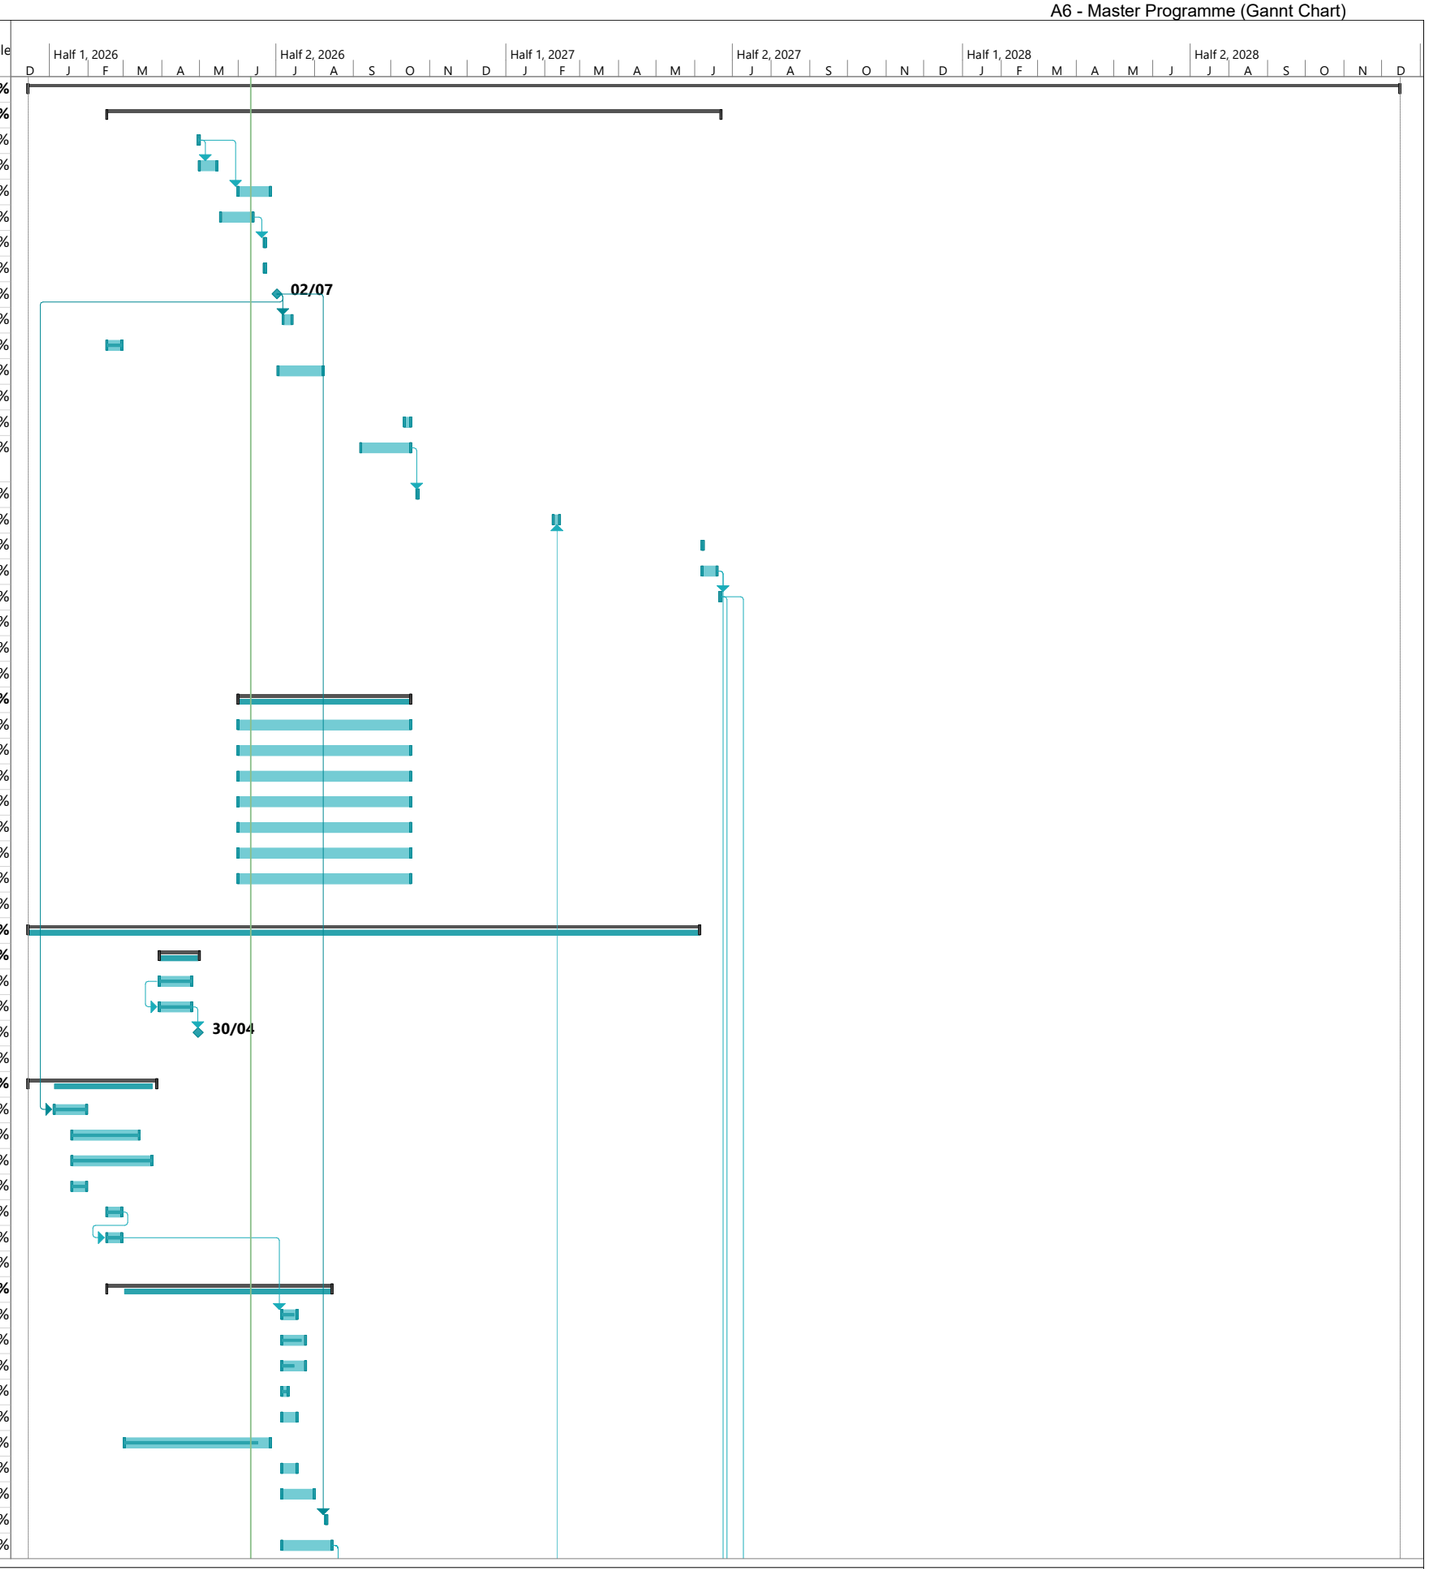

Project: New Arts & Culture Cen
Date: Thu 11/06/26

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Comple
58							0%
59		**Stage 4 Detailed Design**	**210 days**	**Mon 17/08/2(**	**Fri 04/06/27**		**0%**
60		Architectural working drawings & specifications	110 days	Mon 17/08/26	Fri 15/01/27	57	0%
61		Services drawings & specifications	110 days	Mon 17/08/26	Fri 15/01/27	57	0%
62		Agree specialist CDP elements	110 days	Mon 17/08/26	Fri 15/01/27	57	0%
63		Fire strategy drawings	110 days	Mon 17/08/26	Fri 15/01/27	57	0%
64		Interior drawings	110 days	Mon 17/08/26	Fri 15/01/27	57	0%
65		Landscape detail design	110 days	Mon 17/08/26	Fri 15/01/27	57	0%
66		Structural design	110 days	Mon 17/08/26	Fri 15/01/27	57	0%
67		Substructure design	110 days	Mon 17/08/26	Fri 15/01/27	57	0%
68		Stage 4 Design Report	10 days	Mon 18/01/27	Fri 29/01/27	60	0%
69		Stage 4 Cost Plan & PTE	10 days	Mon 25/01/27	Fri 05/02/27	68FS-5 days	0%
70		Tender Documents Preparation	6 wks	Mon 08/02/27	Fri 19/03/27	69	0%
71		Tender Period	6 wks	Mon 22/03/27	Fri 30/04/27	70	0%
72		Tender Assessment vs PTE & budget	4 wks	Mon 03/05/27	Fri 28/05/27	71	0%
73		Tender report & recommendations	1 wk	Mon 31/05/27	Fri 04/06/27	72	0%
74							0%
75		**Planning Application**	**80 days**	**Mon 10/08/2(**	**Fri 27/11/26**		**0%**
76		Submission	1 day	Mon 10/08/26	Mon 10/08/26		0%
77		Planning review	12 wks	Mon 10/08/26	Fri 30/10/26	76	0%
78		Planning Decision	1 day	Mon 02/11/26	Mon 02/11/26	77	0%
79		Conditions Review	4 wks	Mon 02/11/26	Fri 27/11/26	78	0%
80		Receipt of decision notice	0 days	Fri 06/11/26	Fri 06/11/26	78FS+3 days	0%
81		<New Task>					0%
82							0%
83		**Communications**					**0%**
84		Comms Strategy					0%
85		Comms to Working Group - to be agreed					0%
86		Comms to directly impacted stakeholders - tba					0%
87		Comms to indirectly affected stakeholders					0%
88		Comms to Members - tba					0%
89		Press release - tba					0%
90							0%
91		**Procurement & Legal**	**285 days**	**Mon 06/07/2(**	**Fri 06/08/27**		**0%**
92		Procurement Strategy - Techical Design Services for Stage 3/4	6 wks	Mon 06/07/26	Fri 14/08/26		0%
93		Procurement Strategy - Construction	4 wks	Mon 04/01/27	Mon 01/02/27	70SF-1 wk	0%
94		Pre-tender enquiries	2 wks	Mon 08/02/27	Fri 19/02/27	70SS	0%
95		Tender Shortlist	1 wk	Mon 22/02/27	Fri 26/02/27	94	0%
96		Tender Period	6 wks	Mon 22/03/27	Fri 30/04/27	70	0%
97		Tender Assessment vs PTE & budget	4 wks	Mon 03/05/27	Fri 28/05/27	96	0%
98		Tender report & recommendations	1 wk	Mon 31/05/27	Fri 04/06/27	97	0%
99		Governance Review	1 wk	Mon 21/06/27	Fri 25/06/27	98,19	0%
100		Award letters	2 wks	Mon 28/06/27	Fri 09/07/27	20,99	0%
101		Contract documents	4 wks	Mon 12/07/27	Fri 06/08/27	20,100	0%
102							0%
103		**Construction - Stage 5**	**350 days**	**Mon 09/08/27**	**Mon 11/12/28**		**0%**
104		MDC Preparatory Work with Museum	4 wks	Mon 09/08/27	Fri 03/09/27	101	0%
105		Contractor lead-in period & site set-up	4 wks	Mon 09/08/27	Fri 03/09/27	101	0%
106		Partial closure of museum and site clearance	2 wks	Mon 06/09/27	Fri 17/09/27	104	0%
107		Works commence	16 mons	Mon 20/09/27	Fri 08/12/28		0%
108		Contract Progress meeting 1					0%
109		Contract Progress meeting 2 etc.					0%
110		Works complete	0 days	Mon 11/12/28	Mon 11/12/28	107	0%
111							0%
112		**Stage 6/7**	**10 days**	**Mon 04/12/28**	**Fri 15/12/28**		**0%**
113		Handover & Occupation	2 wks	Mon 04/12/28	Fri 15/12/28	110FS-5 day	0%

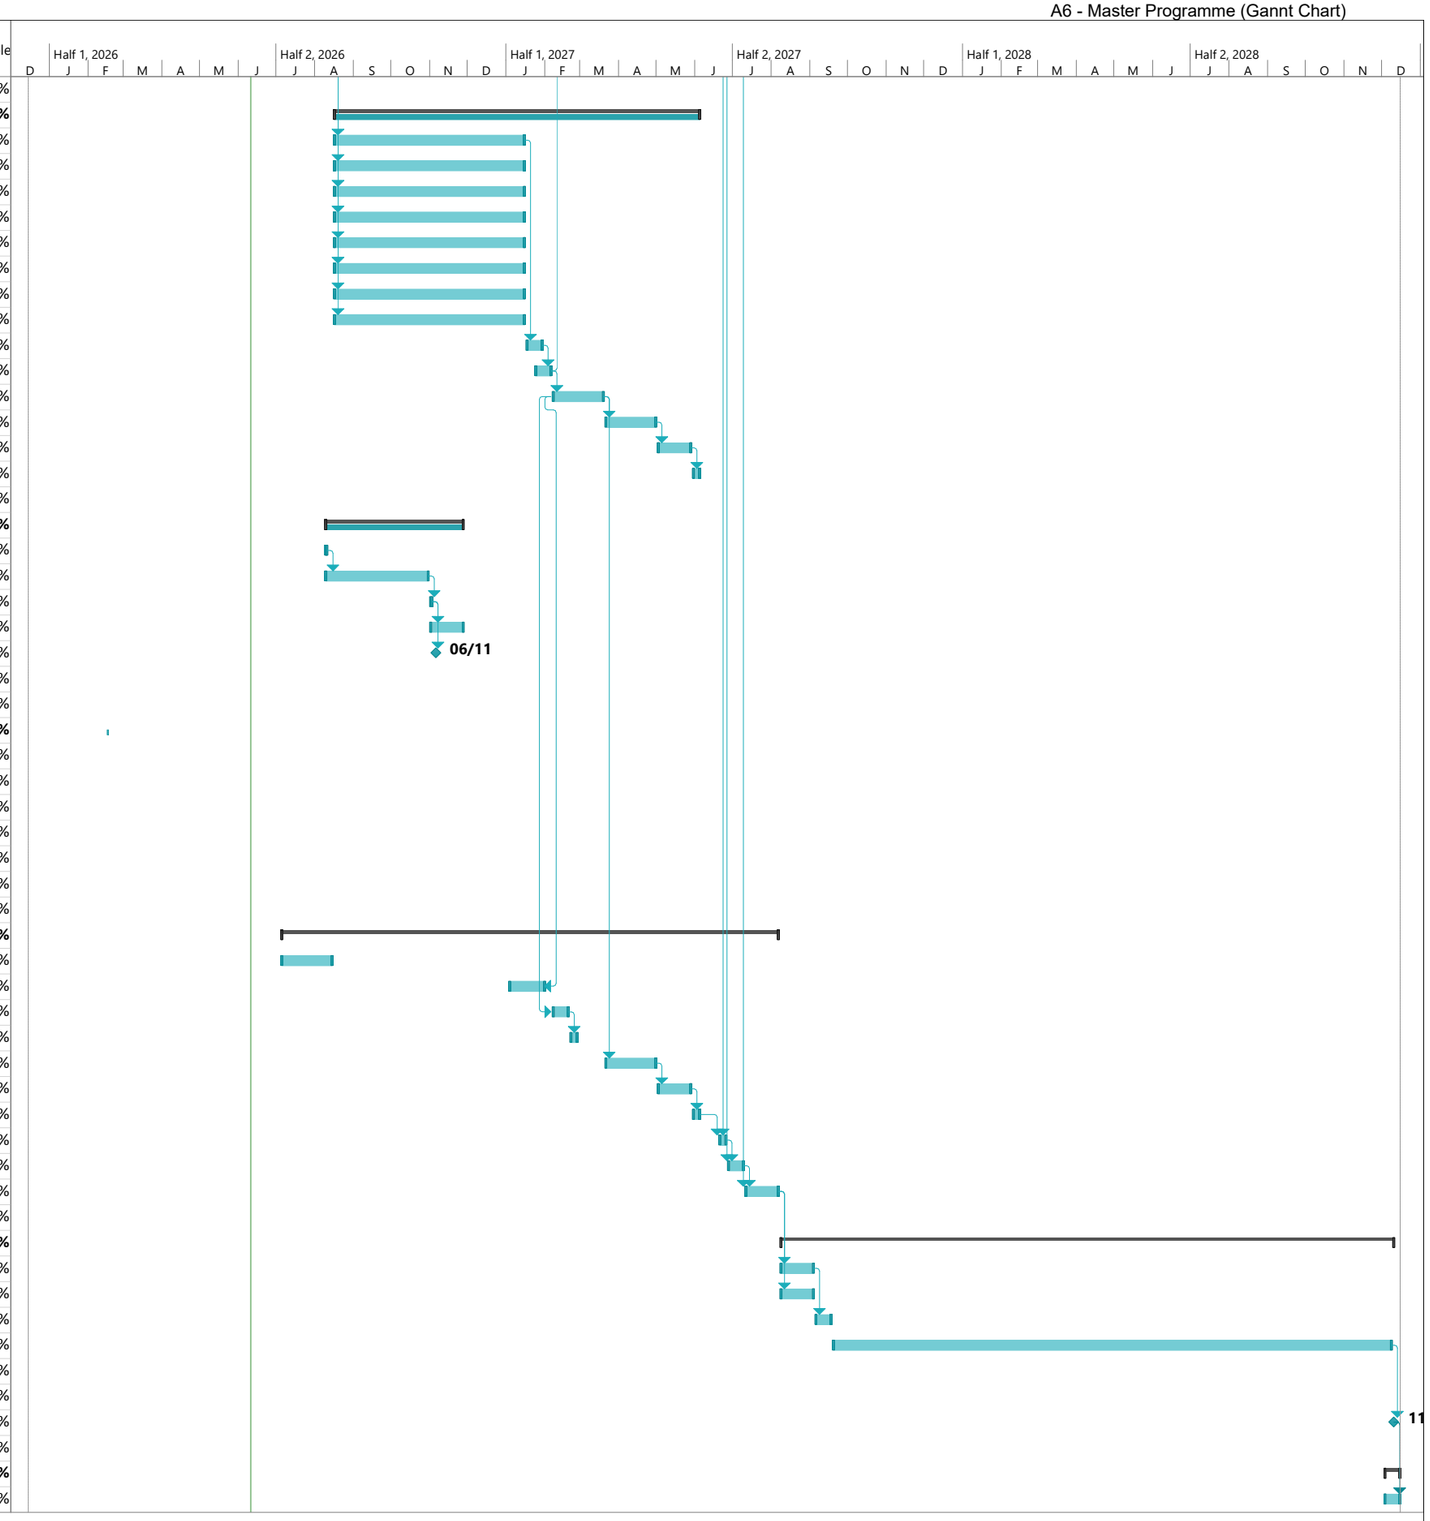

Project: New Arts & Culture Cen
Date: Thu 11/06/26

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
